
TCC PROJECT #8 ANNADALE MODE SHIFT

Project Sponsor:

Self-Help Enterprises

INITIAL ISSUES


- Neighbors fences built into the City Right of Way
- Trees grown in fence at abandoned property

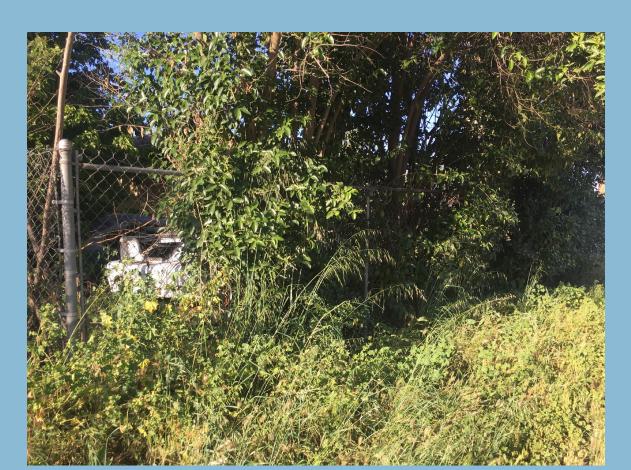



CONCERNS OF COST AND COMMUNITY IMPACT

- Talked with neighbors:
- They were okay with fence moving
- They supported sidewalk
- Preserve Eva's myrtle
- Move Sal's abandoned car
- Worked with Precision to reduce cost in contract

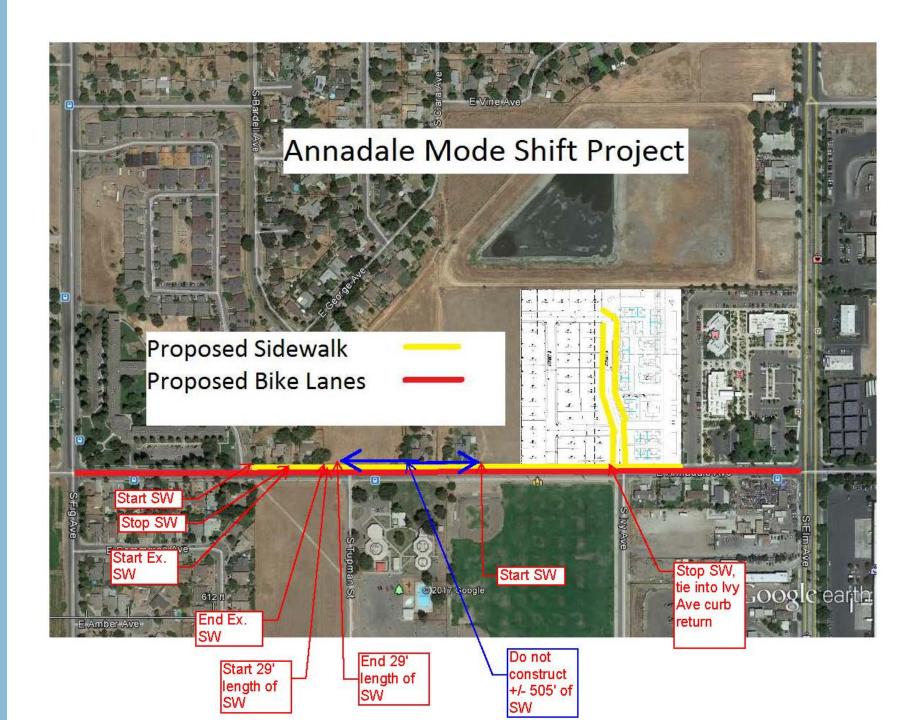

KEEPING THE PROJECT MOVING

Using SHE leverage funds, removed fence and tree work from GC contract

Utilized local contractor (walking distance!) Tony's Fencing for prevailing wage

job to remove and replace fencing outside of ROW

Removed trees

Precision contract now within budget

TCC Grant Amount: \$343,000

+

SHE Leverage Amount: \$150,000

Total Project Cost: \$493,000







COMING MONTHS

- Received final approved plans from City of Fresno Public Works department on 12/15/2020.
- Received approved encroachment permit needed to begin construction on 2/12/2021.
- Will be giving Notice To Proceed to the General Contractor to begin street work in early March 2021.
- Sidewalk and bike lanes should be complete May 2021!

